








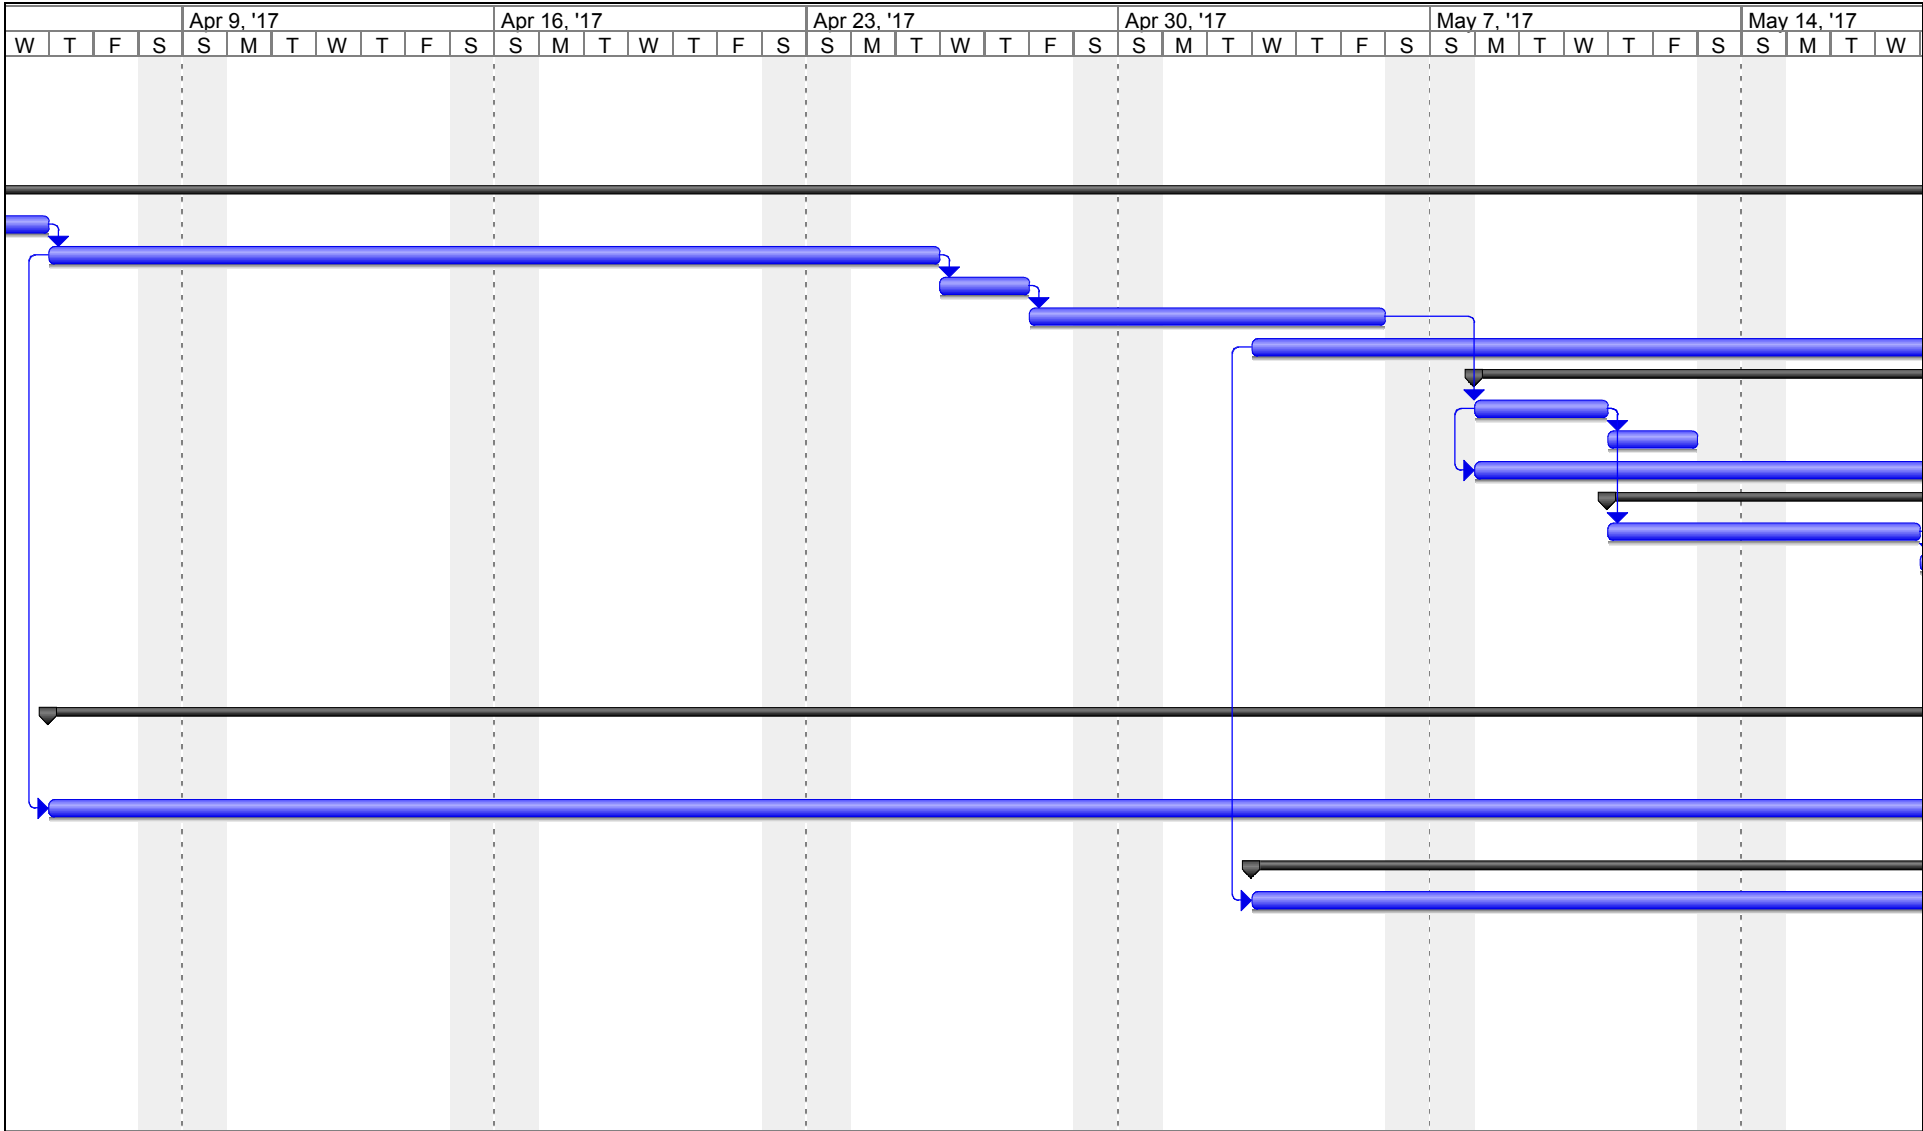


ID	Task Name	Duration	Start	Finish	Predecessors	Mar 19, '17							Mar 26, '17							Apr 2, '17				
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T		
1	<b>Mobilization</b>	<b>10 days</b>	<b>Mon 3/20/17</b>	<b>Fri 3/31/17</b>																				
2	Survey/GPS Set Up	5 days	Mon 3/20/17	Fri 3/24/17																				
3	Mobilize Equipment	3 days	Mon 3/27/17	Wed 3/29/17	2																			
4	EC Measures	2 days	Thu 3/30/17	Fri 3/31/17	3																			
5	<b>Area 1</b>	<b>44 days</b>	<b>Mon 4/3/17</b>	<b>Thu 6/1/17</b>																				
6	Debris Removal	3 days	Mon 4/3/17	Wed 4/5/17	4																			
7	100+00 to 108+20	14 days	Thu 4/6/17	Tue 4/25/17	6																			
8	Overflow Channel	2 days	Wed 4/26/17	Thu 4/27/17	7																			
9	April Rain Days	6 days	Fri 4/28/17	Fri 5/5/17	8																			
10	Trail Closed	22 days	Wed 5/3/17	Thu 6/1/17																				
11	<b>Area 3</b>	<b>66 days</b>	<b>Mon 5/8/17</b>	<b>Mon 8/7/17</b>																				
12	Asphalt Removal	3 days	Mon 5/8/17	Wed 5/10/17	9																			
13	Overflow Channel	2 days	Thu 5/11/17	Fri 5/12/17	12																			
14	Trail Closed	66 days	Mon 5/8/17	Mon 8/7/17	12SS																			
15	<b>Area 2 Third Fork Creek</b>	<b>35 days</b>	<b>Thu 5/11/17</b>	<b>Wed 6/28/17</b>																				
16	200+00 to 203+00	5 days	Thu 5/11/17	Wed 5/17/17	12																			
17	203+01 to 212+38	23 days	Thu 5/18/17	Mon 6/19/17	16																			
18	May Rain Days	7 days	Tue 6/20/17	Wed 6/28/17	17																			
19	<b>Area 2 UT 2A</b>	<b>10 days</b>	<b>Thu 6/29/17</b>	<b>Wed 7/12/17</b>																				
20	300+00 to 301+30	4 days	Thu 6/29/17	Tue 7/4/17	18																			
21	June Rain Days	6 days	Wed 7/5/17	Wed 7/12/17	20																			
22	<b>Area 2 UT 4</b>	<b>89 days</b>	<b>Thu 4/6/17</b>	<b>Tue 8/8/17</b>																				
23	400+00 to 402+62	6 days	Thu 7/13/17	Thu 7/20/17	21																			
24	Site Clean Up	5 days	Fri 7/21/17	Thu 7/27/17	23																			
25	Channel Backfill	55 days	Thu 4/6/17	Wed 6/21/17	7SS																			
26	July Rain Days	8 days	Fri 7/28/17	Tue 8/8/17	24																			
27	<b>Boardwalk</b>	<b>87 days</b>	<b>Wed 5/3/17</b>	<b>Thu 8/31/17</b>																				
28	Begin Driving Piles	22 days	Wed 5/3/17	Thu 6/1/17	10SS																			
29	Boardwalk Constructing	41 days	Fri 6/2/17	Fri 7/28/17	28																			
30	May, June, July Rain Days	21 days	Mon 7/31/17	Mon 8/28/17	29																			
31	Site Clean Up Demobilization	3 days	Tue 8/29/17	Thu 8/31/17	30																			
32	<b>Dormant Season</b>	<b>9 days</b>	<b>Mon 12/4/17</b>	<b>Thu 12/14/17</b>																				
33	Live Stakes	3 days	Mon 12/4/17	Wed 12/6/17																				
34	Riparian Planting, Bare Roots	3 days	Thu 12/7/17	Mon 12/11/17	33																			
35	Herbaceous Plugs	3 days	Tue 12/12/17	Thu 12/14/17	34																			


Project: Third Fork Creek 3-23-17  
Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	







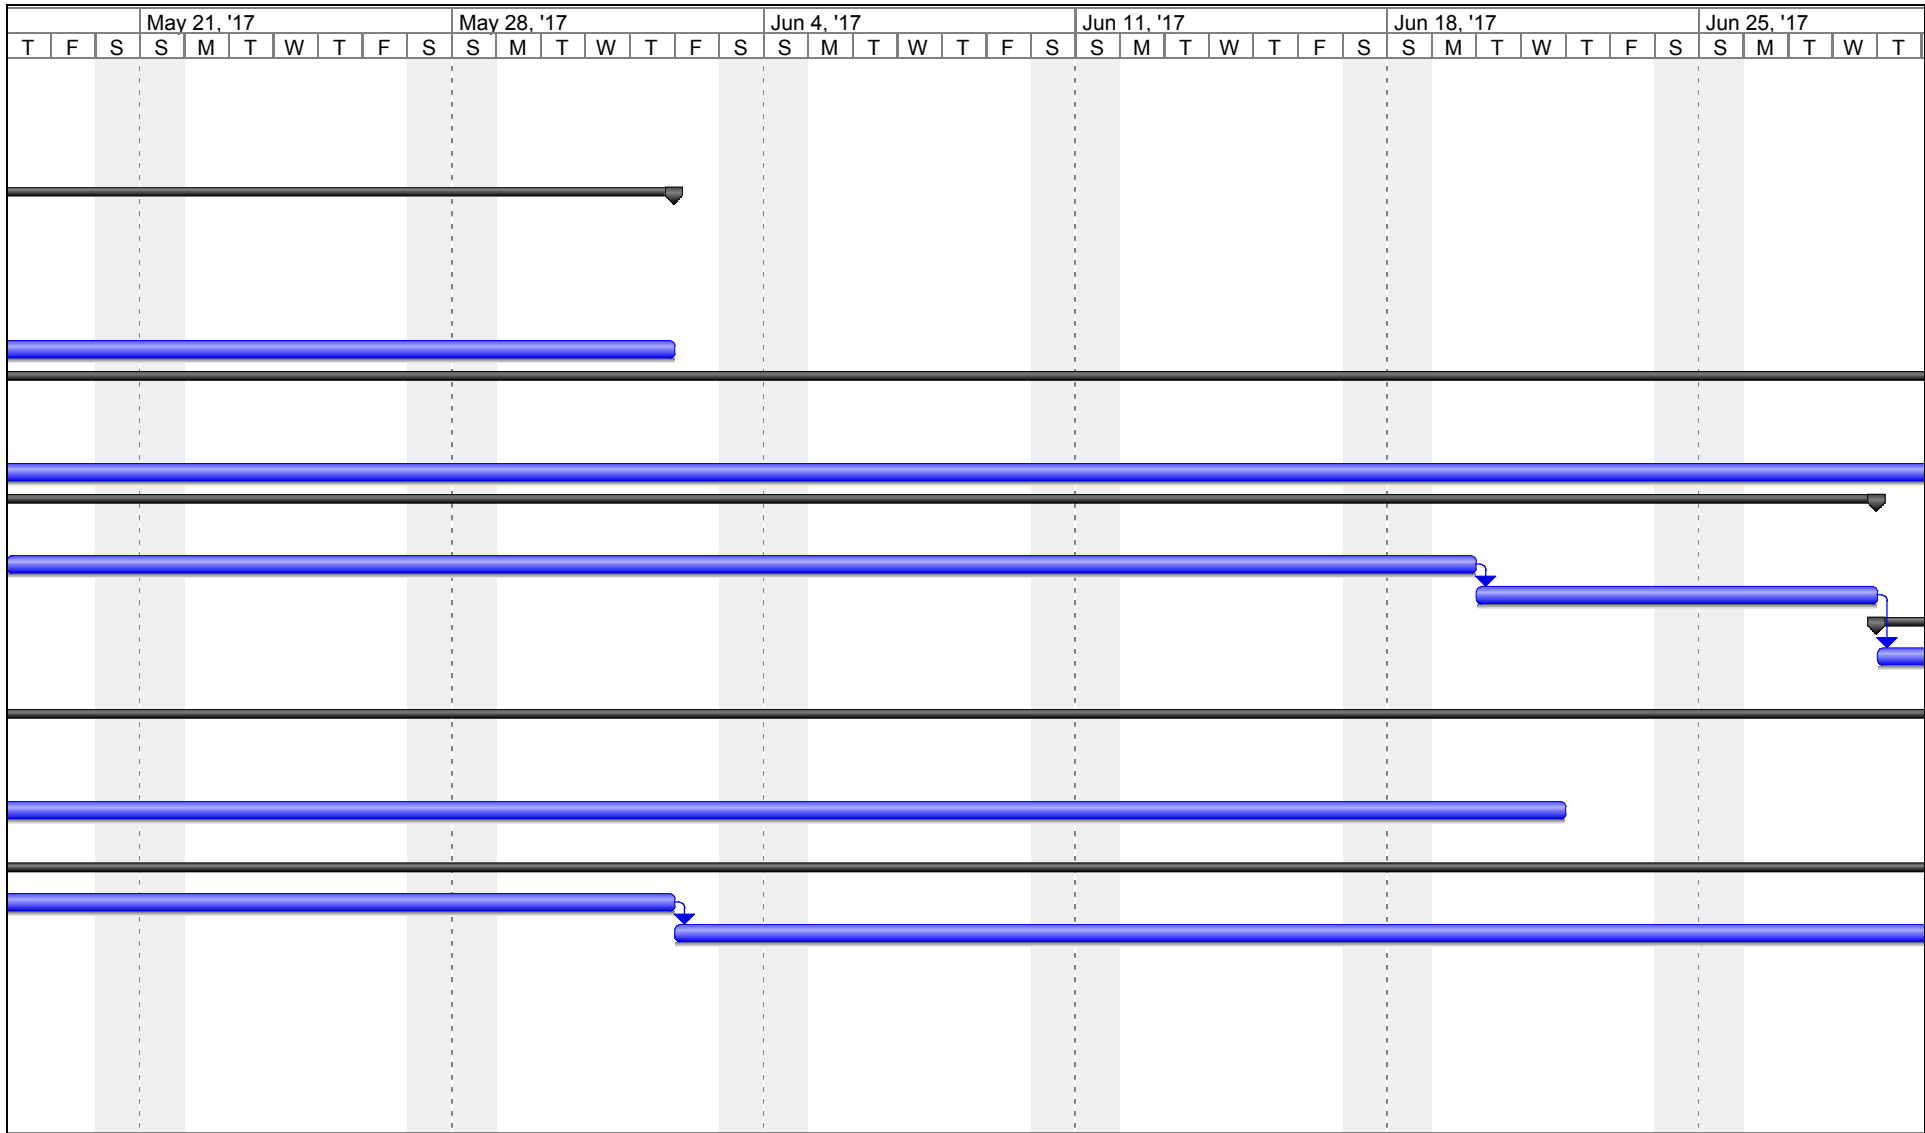




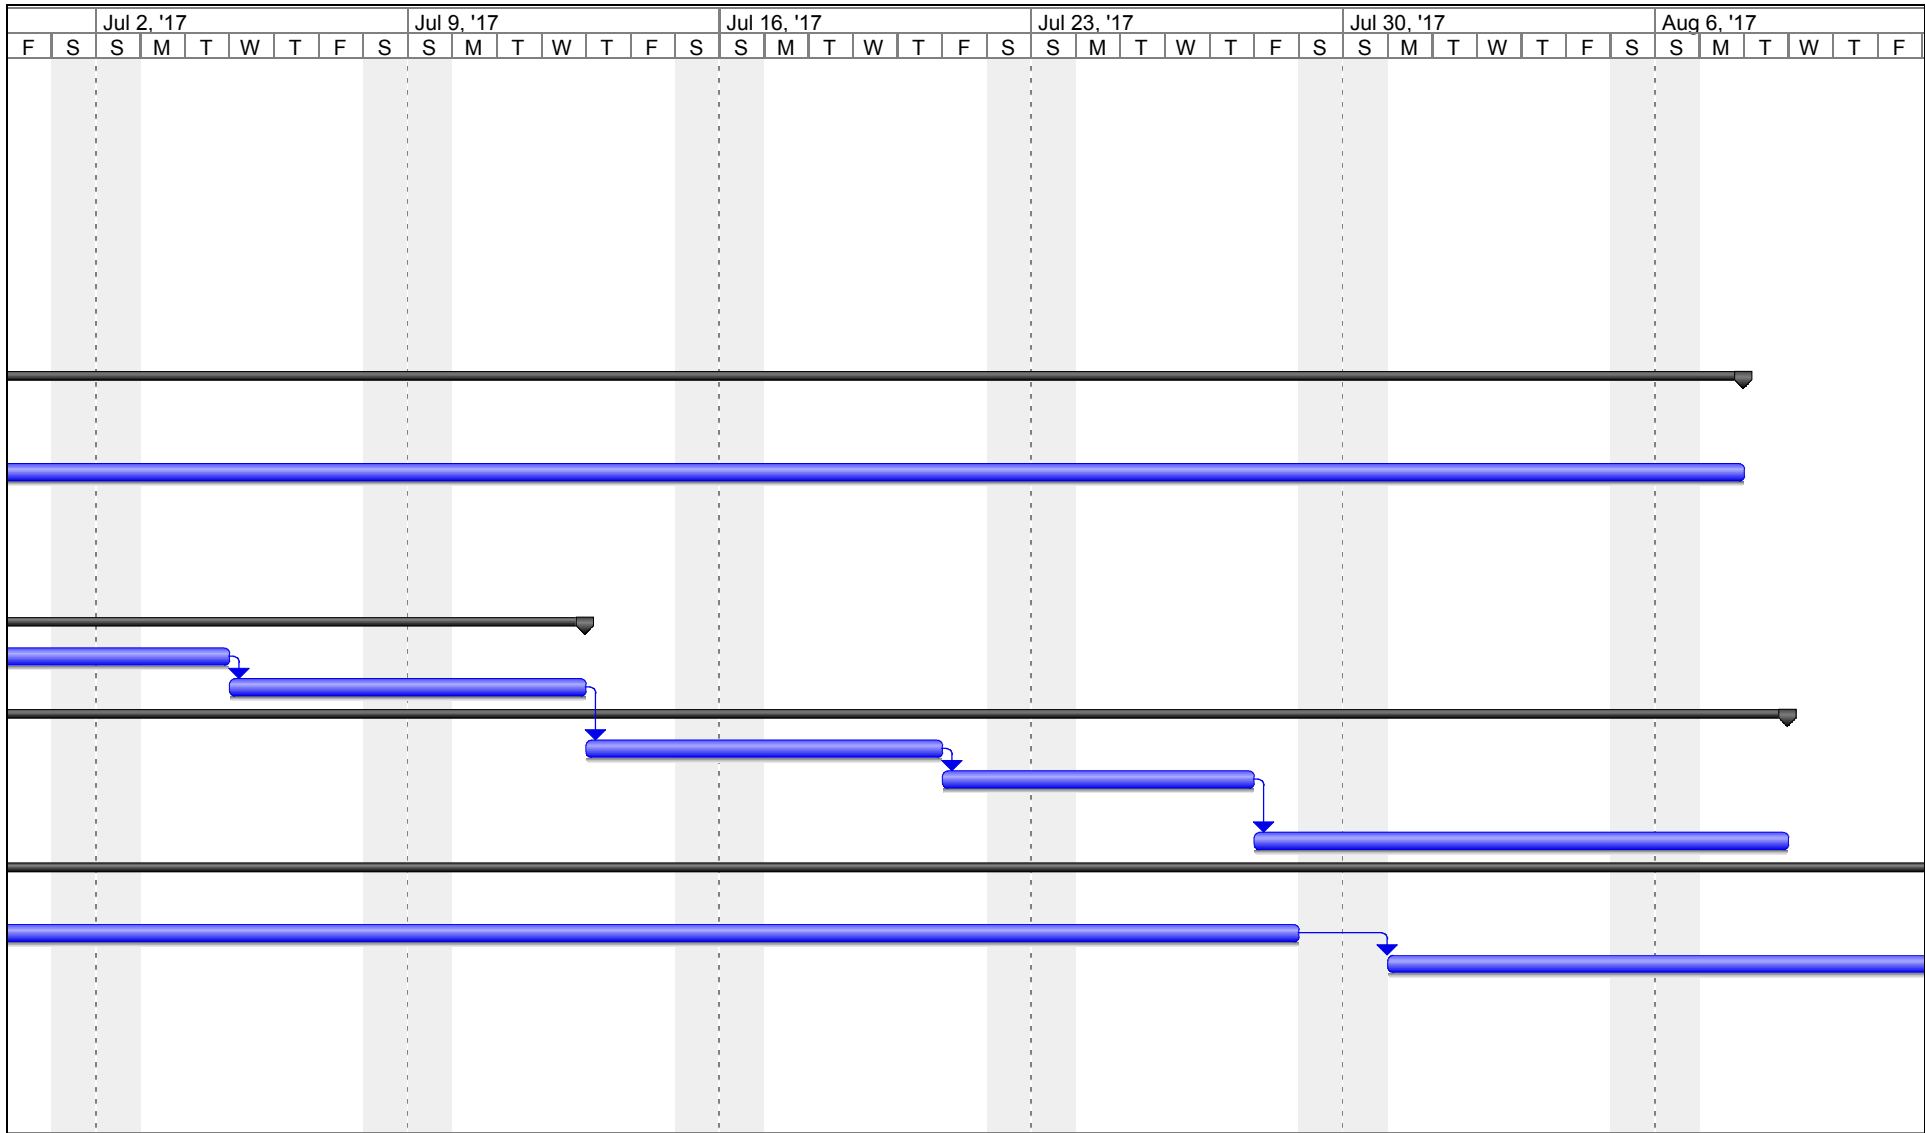
Project: Third Fork Creek 3-23-17  
 Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: Third Fork Creek 3-23-17  
 Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: Third Fork Creek 3-23-17  
Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

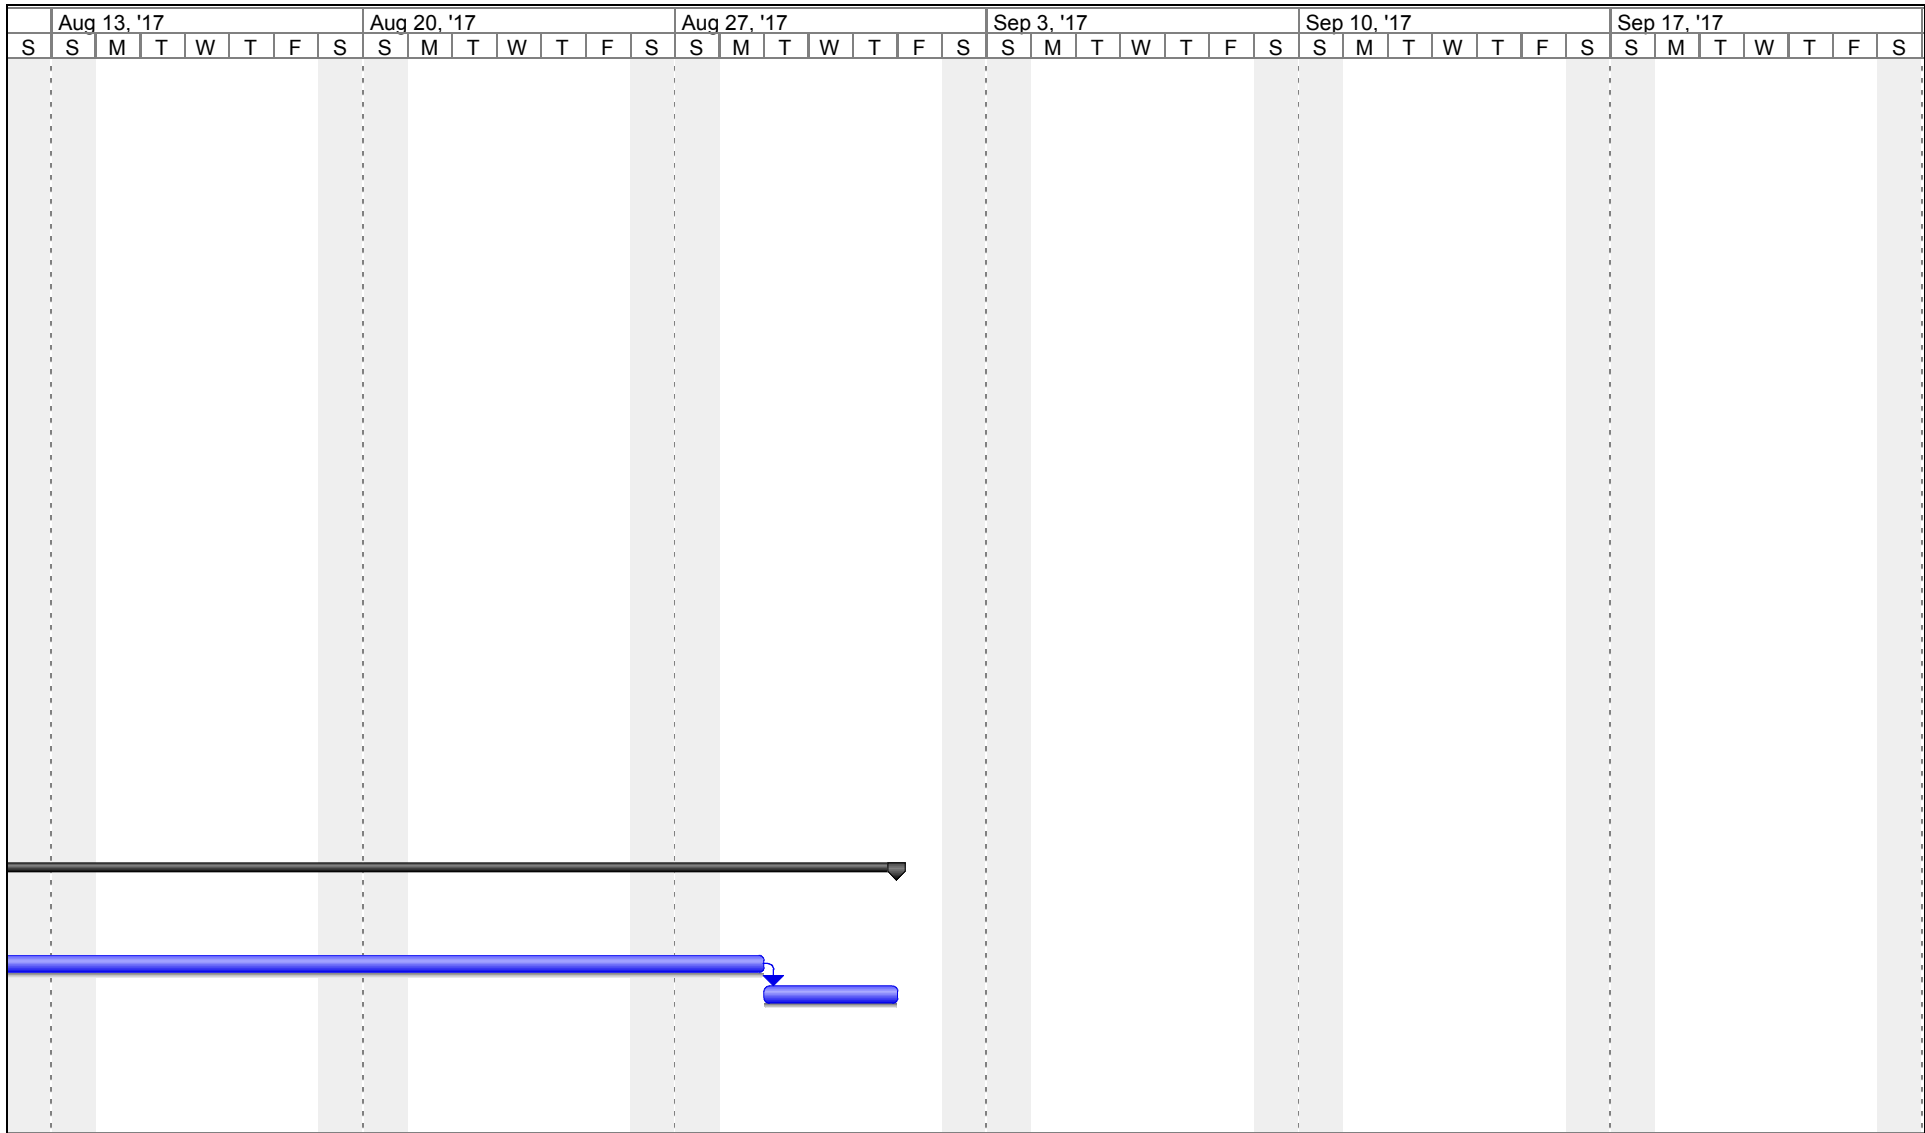










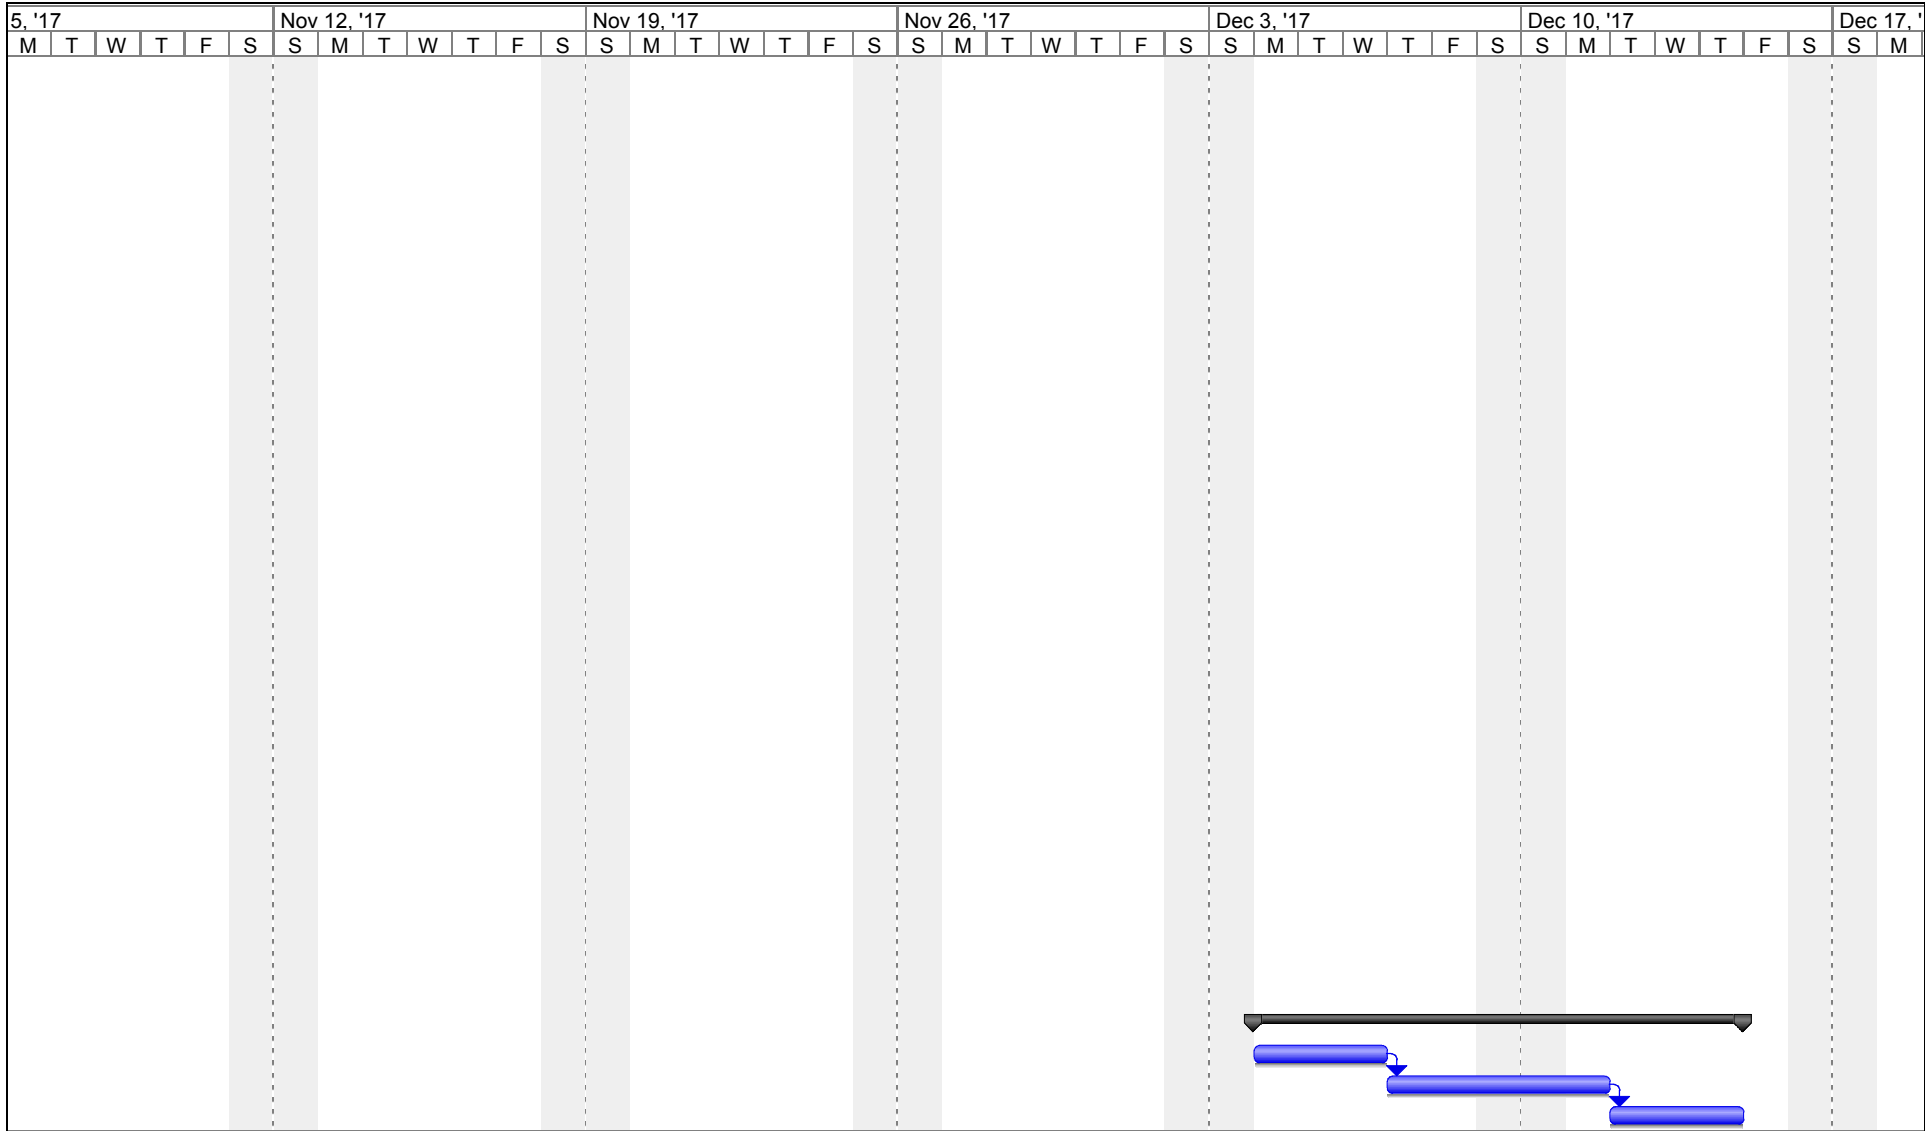
Project: Third Fork Creek 3-23-17  
 Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Third Fork Creek 3-23-17  
 Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Third Fork Creek 3-23-17  
 Date: Thu 3/30/17

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
